

Z O N

WIVENHOE · ESSEX

INVESTMENT PROPOSAL

25 low-carbon homes in three ZON models, 70 minutes from London

INDICATIVE AND NON-BINDING · CONFIDENTIAL

October 2026

INVESTMENT SUMMARY

25 HOMES · £11.47M GDV

25 HOMES	2,786 m² RESIDENTIAL GIA	£9.73m DEVELOPMENT COST	£1.74m PROJECT PROFIT · 15.2%
£2.92m PARTNER CAPITAL	12% TARGET RETURN P.A.	24 MONTHS TERM	70 / 30 SENIOR DEBT / PARTNERS

Private-market case. With a 30% affordable-housing obligation, project profit falls to about £0.46m.



THE SITE

CROQUET GARDENS

Item	Detail
Area	3.52 acres · freehold
Planning	Outline: 25 bungalows + 60-bed care
Transport	Station 0.7 miles · London 70 min
Flood risk	Zone 1 · SuDS drainage
Location	Wivenhoe, Colchester, Essex

Masterplan for reference. A measured CAD schedule will confirm plots, roads, parking, drainage and biodiversity.


CHAPEL HOUSE
ESTATE
MODERN LIVING
IN HARMONY
WITH NATURE
SUSTAINABLE
MATERIALS
ENERGY
EFFICIENT
MODERN
DESIGN
A HEALTHIER
HAPPIER YOU
THE CONCEPT
A VILLAGE,
NOT AN
ESTATE
Quiet lanes with no through traffic, private hedged gardens and homes built off-site by ZON with heat pumps and solar PV.

ZON HOMES

THREE MODELS



LAKE HOUSE COMPACT

2 bedrooms · 2 bathrooms · single storey

9.0 × 7.5 m



LAKE HOUSE

2 bedrooms + study · 2 bathrooms · single storey

92 m² · 14 × 8 m



RESIDENCE

4 bedrooms · 2 bathrooms · two storeys

Family home with utility and WC

CGI concepts. Floor plans follow.



2 BEDROOMS · SINGLE STOREY


LAKE HOUSE COMPACT

9.0 × 7.5 m 2 bedrooms · 2 bathrooms Kitchen-living 28.5 m²

FLOOR PLAN

LAKE HOUSE COMPACT

Open kitchen-living with dining, two bedrooms, two bathrooms, a plant room and an entrance with storage.

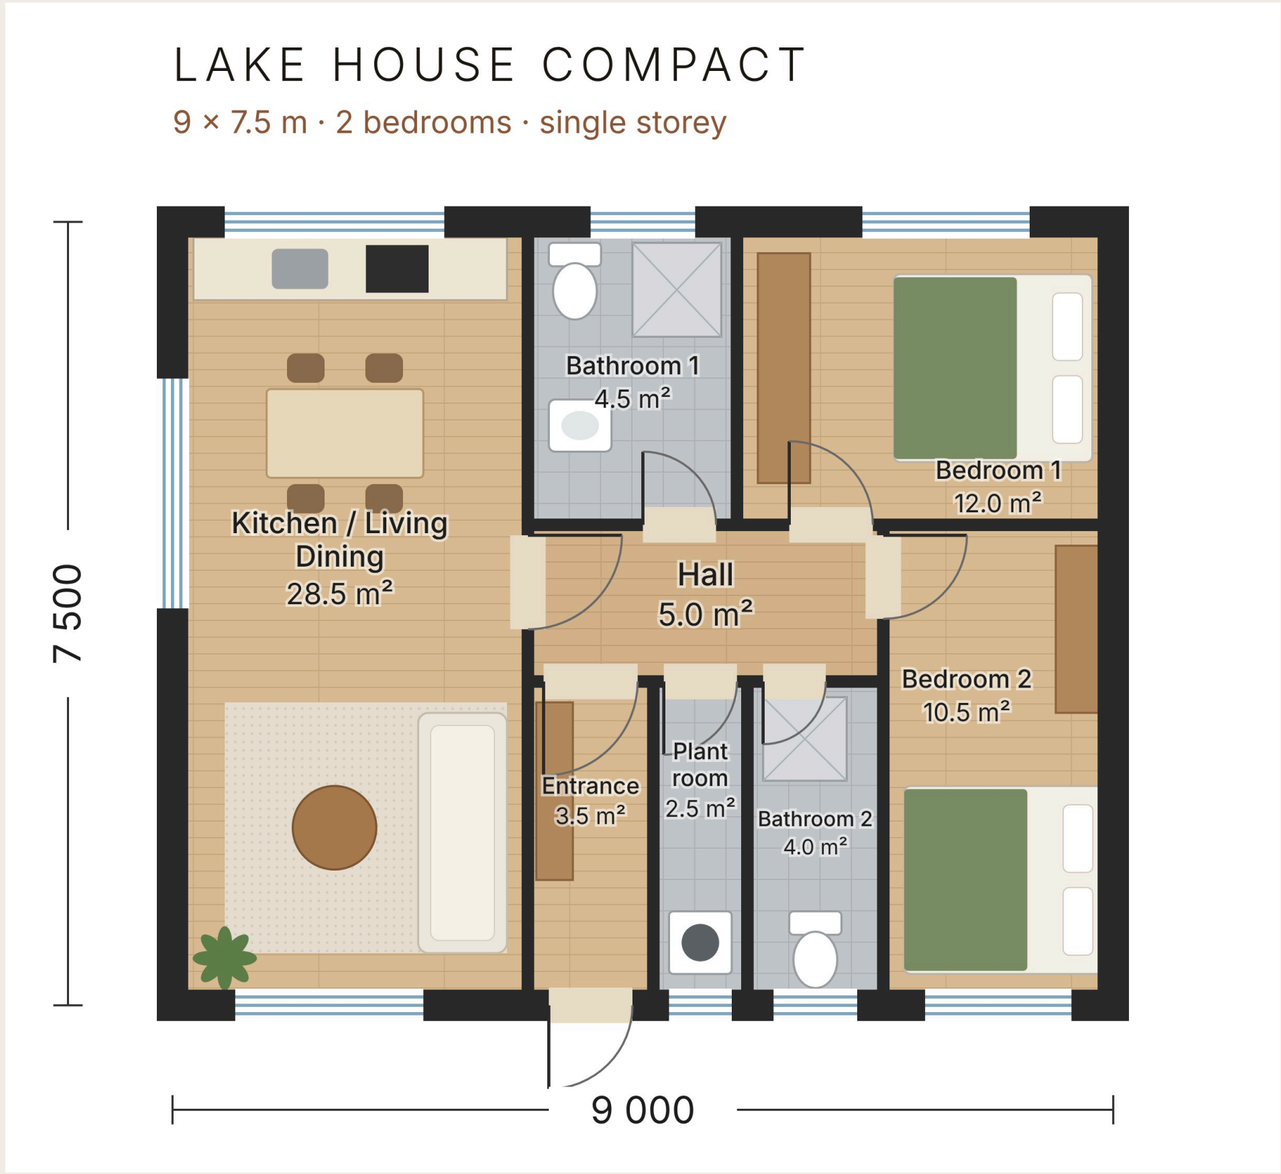



2 BEDROOMS + STUDY · SINGLE STOREY

LAKE HOUSE

92 m² · 14 × 8 m 2 bedrooms + study · 2 bathrooms Kitchen-living 26 m²


FLOOR PLAN

LAKE HOUSE

Study, walk-in wardrobe and two bathrooms on one level

LAKE HOUSE

92 m² · 2 bedrooms + study · single storey

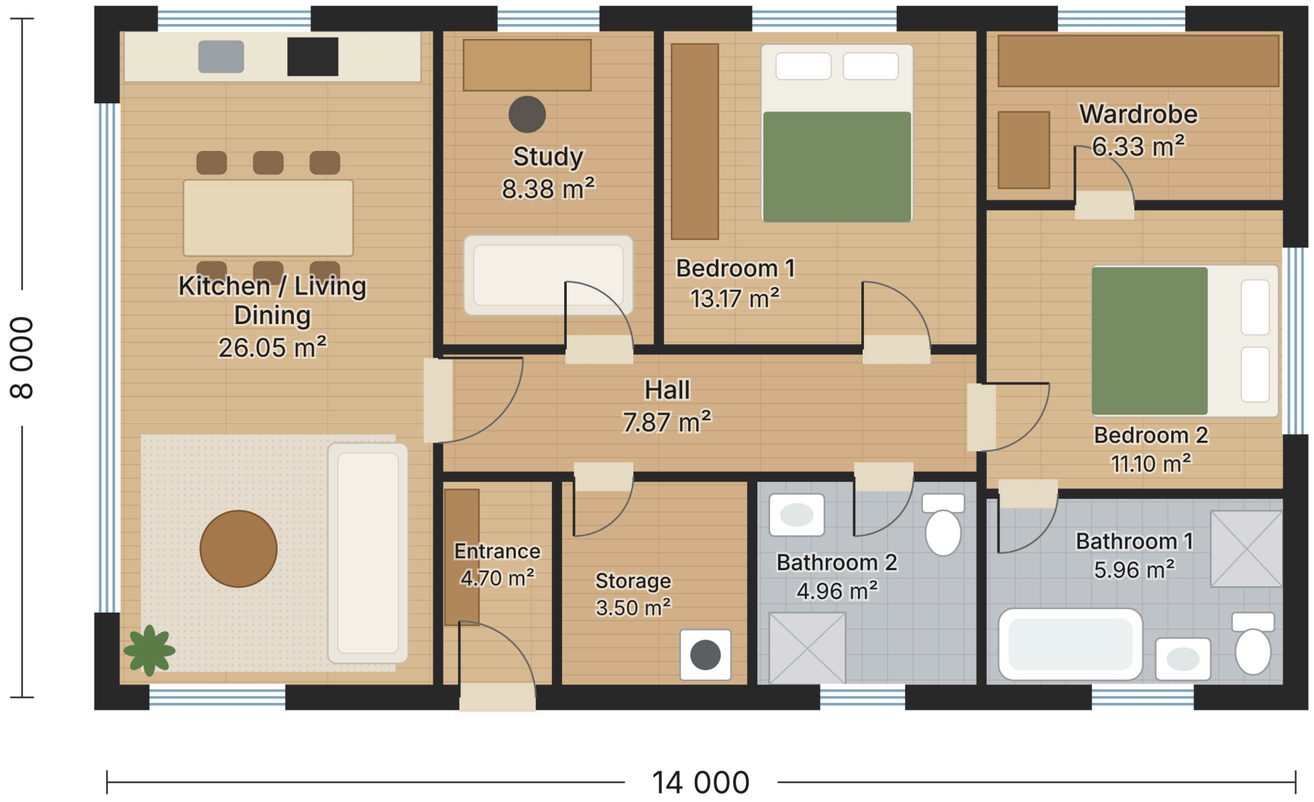



4 BEDROOMS · TWO STOREYS

RESIDENCE

Living, dining and kitchen

4 bedrooms · bathroom · shower room

Utility · WC · storage


FLOOR PLANS

RESIDENCE

Living on the ground floor, four bedrooms upstairs


RESIDENCE · GROUND FLOOR

Two storeys · 4 bedrooms

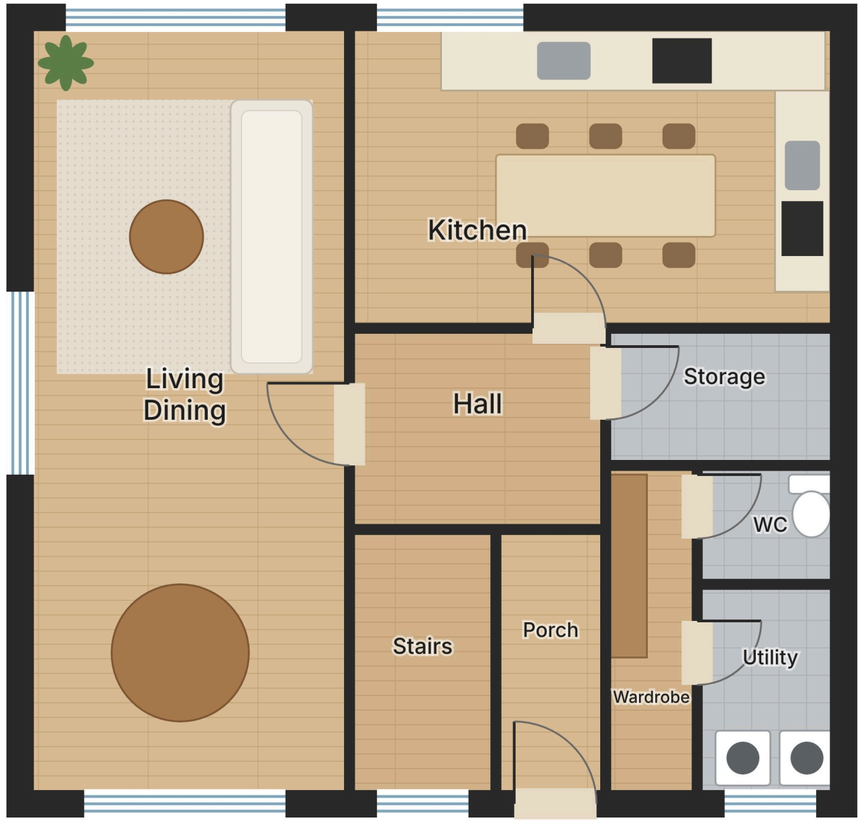

RESIDENCE · FIRST FLOOR

4 bedrooms · 2 bathrooms

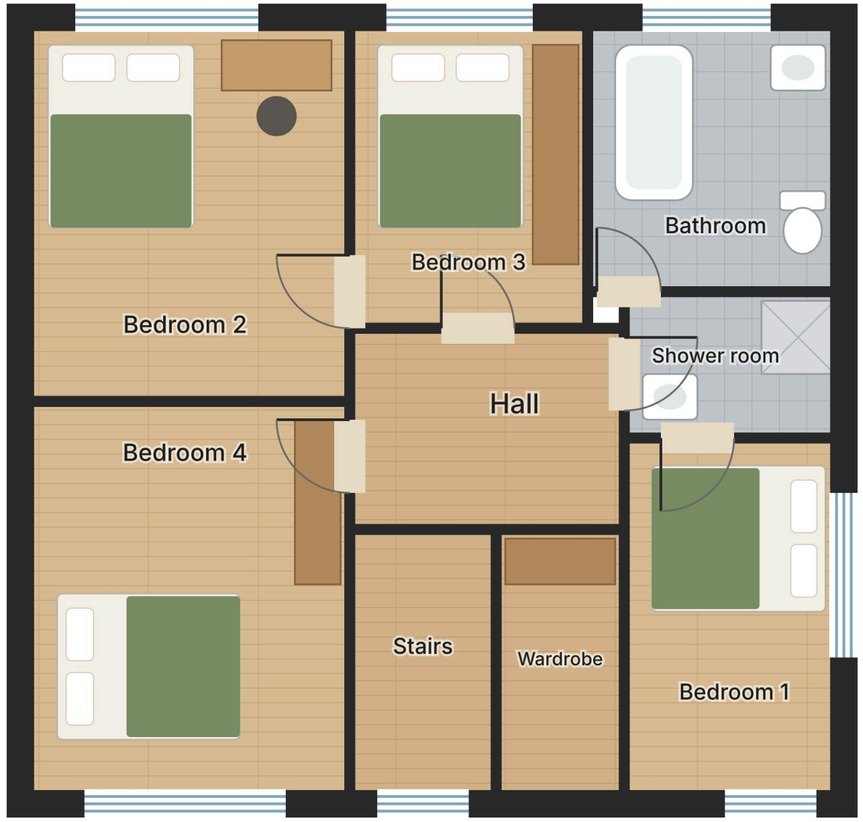

DESIGN &
ARCHITECTURE



GROUND FLOOR

DESIGN &
ARCHITECTURE



FIRST FLOOR

INTERIORS

LIGHT, SPACE AND QUIET







Heat pump, underfloor heating and solar PV keep running costs low. CGI concepts.

DEVELOPMENT BUDGET

£9.73M TOTAL

£1,700 per m² as the full residential construction cost. External works, fees, planning obligations, sales, land and finance shown separately.

Use of funds	Amount	Share
Land	£1,500,000	15.4%
SDLT and land legal costs	£90,000	0.9%
Construction of 25 homes	£4,736,200	48.7%
External works and utilities	£875,000	9.0%
Contingency	£280,560	2.9%
Professional fees	£561,120	5.8%
S106, RAMS and off-site BNG	£429,000	4.4%
Marketing, agents and sales legal	£324,250	3.3%
Finance	£934,752	9.6%
Total development cost	£9,730,882	100%

Land value of £1.5m is a placeholder until the purchase price or option terms are agreed.

FUNDING STRUCTURE

PARTNERS PAID BEFORE ZON

01 · SENIOR LENDER

£6.81m

70% of cost. Repaid first from sales, with interest.

02 · PARTNERS

£2.92m

30% of cost. Capital plus a target 12% p.a. preferred return.

03 · ZON

Residual

No distributions to ZON before partners are repaid.

Initial tranche up to £0.80m: land, planning, surveys

Construction tranche up to £2.12m: after term sheet and QS plan

PROFIT WATERFALL

TWO CASES

Measure	Private market	30% affordable
Development value	£11,470,000	£10,158,000
Total development cost	(£9,730,882)	(£9,695,130)
Project profit before partner return	£1,739,118	£462,870
Partner preferred return (12% · 24 months)	(£700,624)	(£462,870)
Residual profit to ZON	£1,038,494	£0
Cover of partner return	2.48×	0.66× · £237,754 short

The investment case depends on the final affordable-housing requirement, confirmed with the council before funding.

RISKS AND CONTROLS

EVIDENCE BEFORE CAPITAL

Risk	Control
Affordable housing	Confirm S106 terms and indicative RSL transfer values before funding
Land price	Conditional contract or option, price capped against residual value
Sales values	Two written local agent opinions and an independent Red Book valuation
Construction cost	QS cost plan and fixed-price scope confirming £1,700/m² and exclusions
Planning	Confirm the two-storey Residence within the bungalow consent
Site capacity	Measured CAD schedule for plots, roads, parking, SuDS and BNG
Sales timing	Phased build, reservations monitored before main construction

PROGRAMME

24 MONTHS

Months 0–3

DEAL

Land agreement, due diligence, funding terms

Months 3–9

CONSENT

Planning, engineering, valuation, procurement

Months 9–18

BUILD


Groundworks, manufacturing, assembly

Months 15–24

SALES

Completions, sales and repayment

Indicative until the planning route, construction programme and lender drawdown conditions are confirmed.

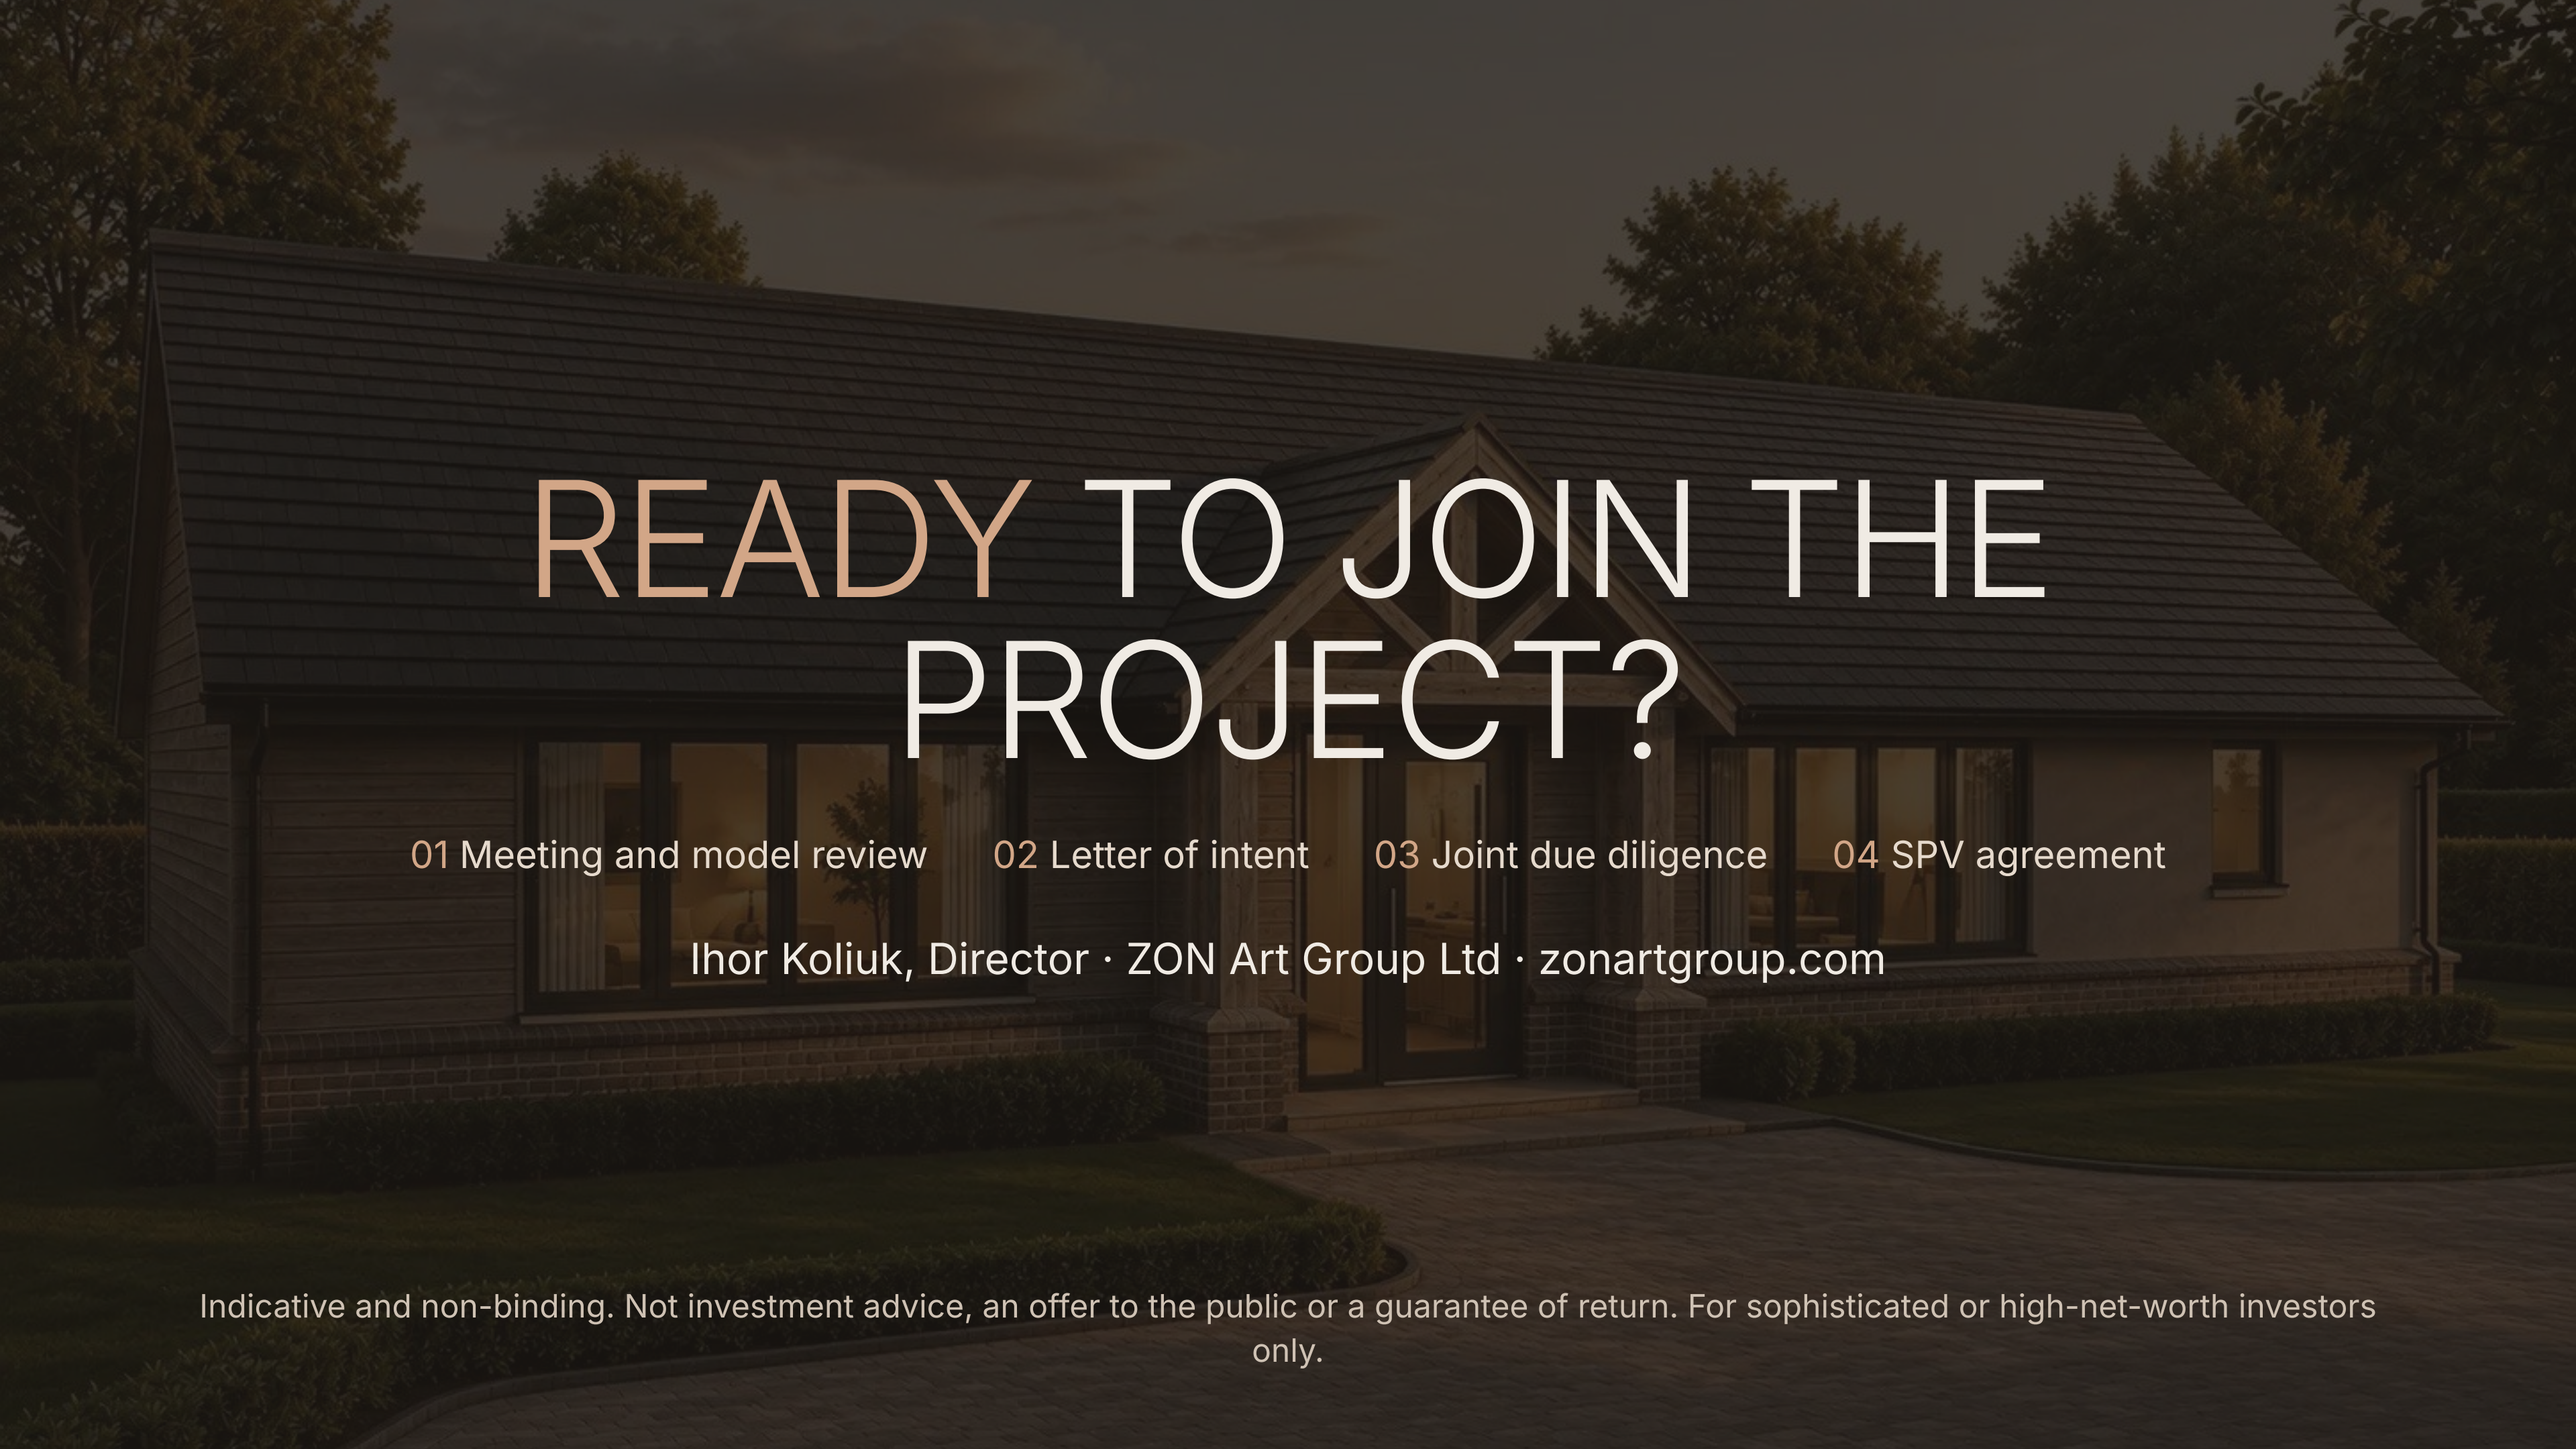

READY TO JOIN THE PROJECT?

01 Meeting and model review 02 Letter of intent 03 Joint due diligence 04 SPV agreement

Ihor Koliuk, Director · ZON Art Group Ltd · zonartgroup.com

Indicative and non-binding. Not investment advice, an offer to the public or a guarantee of return. For sophisticated or high-net-worth investors only.
